



**Project Status Summary:**

Procurement of Professional Services:

- A/E Services Tranche II - A/E interviews underway, target selection and award by April 2017.
- CM Services Tranche II - RFP presented for approval 2.23.17; anticipate issuance of document in March 2017.

Financial Plan:

- Working with JSCB staff and district financial advisors to identify key milestones related to required project approvals (multiple parties), submission of revised financial plan, and permanent financing.

Project Design Status:

- Design Development Documents completed in February 2017. Construction management firms are developing cost estimates. Per the requirements of the legislation the schematic design documents and cost estimates were submitted to SED on 2.10.17 for their review. Meeting held with SED on 2.14.17 to discuss cost allowances and clarify qualifying work criteria. SED is reviewing presented material and will formulate comments and or required corrections.

**Schedule Update:**

- Schematic Design submission was issued to SED on 2.10.17. Targeting design development submission to SED at the end of March. Currently anticipate having SED approval in 1st quarter of 2017 with procurement in the 4th quarter of 2017 and 1st quarter of 2018.

**Constraints / Critical Issues:**

- Develop GC / Prime Contract Form
- Adopt Master Schedule Key Milestones Tranche II
- Completion of Tranche II work will extend beyond the original comprehensive plan completion date of second quarter 2020 - Change conditions and potential to be reviewed.
- Design work at Blodgett is on a temporary hold - resolution required
- Determine engineered solution to stabilize unsuitable soils to enable construction of track and field at Fowler HS.

**Project Cost to Date:**


Total Budget:	\$291,500,000.00
Total Cost Incurred to Date):	\$ 3,211,816.95
Total Percentage complete:	.011%

**February Fun Fact:**

Syracuse gets hit by three major types of snowstorms: nor'easters, lake effect, and Alberta clippers.



\*Source: Syracuse.com

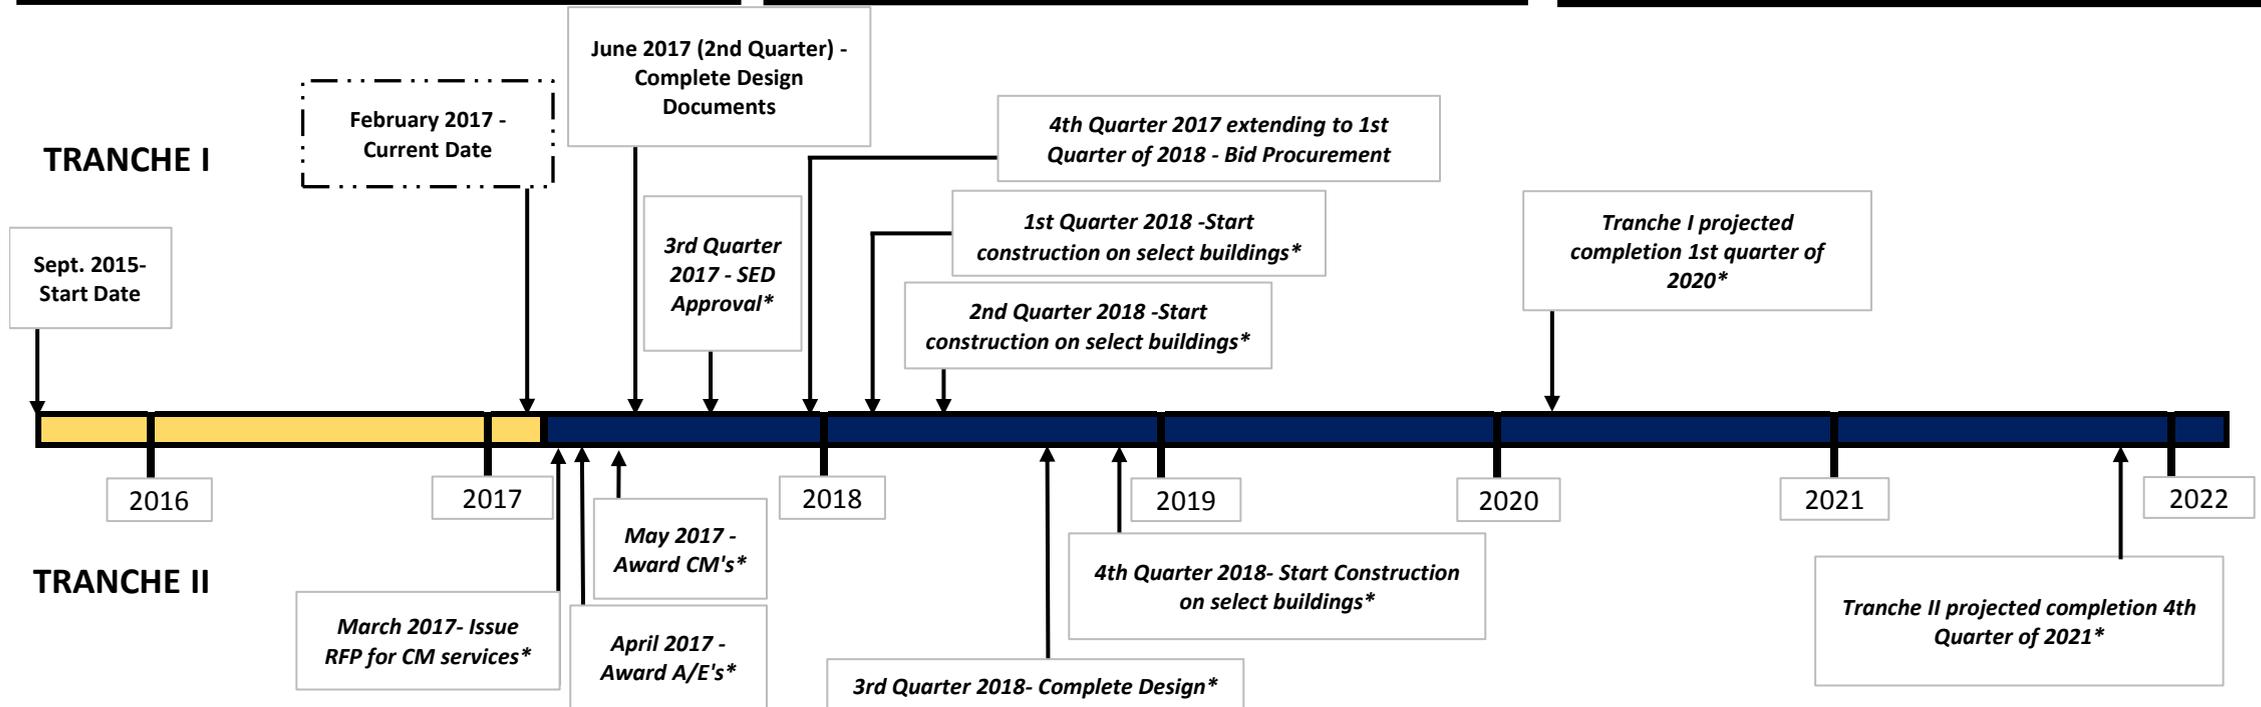

\* Estimated date to be confirmed
